Department of Computer Science & Engineering

University of Dhaka

Abhijatri

A Bangla-First, Offline-Ready Community Travel Platform for Bangladesh

Project Proposal

CSE 3102: Software Development Project

Submitted to	Palash Roy, Lecturer, Department of CSE
Team	ChoturMatra
Project type	Software development
Platform	Bangla-first, offline-ready Progressive Web Application (PWA)
Proposal date	12 October 2026
Final completion	17 or 18 January 2027

Team Members

Responsibility	Member	Roll	Primary contribution
Project leader	Shahriar Islam	61	Scope control, content, estimator rules, administration, integration, and documentation
Frontend and offline	Abdullah Bin Sorwar Choudhury	22	React, TypeScript, bilingual interface, PWA, and offline packs
Backend and data	Syed Muhtasim Alam	04	FastAPI, PostgreSQL, authentication, APIs, rating, and idempotency
Software quality assurance	Md. Irfan Iqbal	35	Test strategy, validation, real-device testing, pilot, and regression

Contents

Scope Decision **1**

1 Executive Summary **1**

2 Problem Statement **1**

2.1 Fragmented travel information 1

2.2 Unclear trip costs 1

2.3 Weak connectivity 1

2.4 Limited Bangla-first support 2

2.5 Trust, moderation, and freshness 2

3 Objectives and Goals **2**

4 Functional Requirements **3**

4.1 Core Product Features 3

4.2 Future Product Features 3

4.3 User Roles 4

4.4 Functional Requirement Catalogue 4

4.5 Abhijatri Cost Planner 5

4.6 Primary Use Cases 8

4.7 Representative User Stories 10

4.8 MVP Exclusions 10

5 Non-functional Requirements **10**

6 Stakeholders **11**

7 Timeline and Milestones **12**

7.1 Formal Testing Phase 12

7.2 Progress Reporting 13

7.3 Project Gantt Chart 13

8 Risk Assessment **17**

9 Feasibility Study **18**

9.1 Technical Feasibility 18

9.2 Economic and Financial Feasibility 18

9.3 Schedule and Time Feasibility 18

9.4 Operational and Ethical Feasibility 19

9.5 Feasibility Conclusion 19

List of Figures

1 Abhijatri system use case model (UML). Packages 4 and 6c are demonstration-only. 9

2 Implementation Gantt chart, part 1 of 3: foundation and first major feature (M1) 14

3 Implementation Gantt chart, part 2 of 3: cost estimator, 50–60% checkpoint (M2), and hardening 15

4 Implementation Gantt chart, part 3 of 3: formal testing (M3) and final completion (M4) . . 16

List of Tables

1 Project objectives and completion measures. 2

2 User roles and permitted actions 4

3 Functional requirement catalogue 4

4 Cost planner inputs and their effect on the calculation. 5

5 Quantity and period rules by pricing unit 6

6 Worked example of the cost calculation (indicative prices, BDT) 7

7 Derivation of category confidence for the worked example 7

8 Scope of the use case model 8

9 Representative user stories with requirement traceability 10

10 Non-functional requirements and acceptance measures 10

11 Stakeholders, interests, and engagement 11

12 Fixed milestones and acceptance evidence 12

13 Formal testing activities and required records 12

14 Schedule summary by phase 13

15 Primary-owner workload balance 13

16 Risk register with early warnings and mitigation 17

17 Semester cost allowance 18

Scope Decision

Abhijatri will be developed as a Bangla-first, offline-ready Progressive Web Application. The semester minimum viable product (MVP) is organised around one complete journey: a traveller explores a destination, generates a contextual cost estimate, downloads an offline travel pack, and submits a moderated review after reconnecting. Vendor commerce, real payments, group tours, and tourmate matching are future phases. A reservation and payment sandbox may be demonstrated only as a non-production extension; it is not part of semester acceptance.

1 Executive Summary

Travellers in Bangladesh often plan trips from social media posts, agency advertisements, personal blogs, maps, and informal recommendations. These sources vary in age, format, and reliability. They rarely explain why two trips to the same destination have different costs, and they become difficult to use when network access is weak.

Abhijatri is a community-driven travel platform designed for Bangladesh. It combines bilingual destination guidance, structured community reviews, transparent ratings, dated travel advisories, an explainable rule-based cost planner, and downloadable offline travel packs. Bangla is the default language; English is available through a persistent language control.

The semester outcome is a tested PWA with five seeded destination profiles: Cox's Bazar, Sajek, Sylhet, the Sundarbans, and Bandarban. The final demonstration will cover the destination, estimate, offline, review, and moderation flow. The platform will not use machine learning for cost prediction. It will use documented pricing rules, source dates, pricing units, season factors, low–expected–high ranges, and confidence labels.

2 Problem Statement

2.1 Fragmented travel information

Travel information for Bangladesh is distributed across many platforms. Users must compare content with different dates, assumptions, and commercial interests. Seasonal restrictions, permits, transport changes, verified contacts, and local guidance can be missed.

2.2 Unclear trip costs

A single average cannot represent a solo traveller, student, couple, family, or group. Accommodation can be priced per room, transport per person or per vehicle, meals per person, and guides per group or per day. A useful estimate must show the cost basis, the traveller context, and the source date.

2.3 Weak connectivity

Hill districts, rural areas, and remote destinations may have slow, unstable, or unavailable mobile data. Travellers can lose access to contacts, guidance, advisories, and cost details exactly when they need them. An online-only system does not meet this requirement.

2.4 Limited Bangla-first support

International travel services may provide reviews and maps, but they do not consistently provide Bangla-first guidance, Bangladesh-specific pricing units, local seasonality, and contextual cost explanations in one workflow.

2.5 Trust, moderation, and freshness

Community content can be duplicated, biased, or manipulated. Prices and travel restrictions also change. The system must show review counts, moderation status, source dates, confidence labels, and advisory validity. Expired information must not be presented as current.

3 Objectives and Goals

Each objective is measurable against the final completion date.

Table 1. Project objectives and completion measures

ID	Objective	Completion measure
O1	Deliver a bilingual PWA	Bangla-default interface, persistent English selection, and installable application shell
O2	Publish seeded destination profiles	Five profiles with bilingual guidance, dated sources, contacts, seasonality, and advisories
O3	Provide explainable cost estimation	Itemised BDT estimate with pricing units, low–expected–high range, per-person cost, source dates, and confidence label
O4	Provide dependable offline access	Every completed pack download opens successfully in 10 of 10 airplane-mode tests
O5	Implement trustworthy reviews	Structured reviews, offline drafts, moderation states, reporting, and duplicate-safe submission
O6	Evaluate estimator performance	Ten held-out trips evaluated after the seed catalogue is frozen, without tuning on those trips (Section 4.5.6)
O7	Validate usability	At least eight consenting participants, including a Bangla-preferring user and a less technical user
O8	Meet the reporting schedule	Biweekly evidence-based progress reports, formal testing from 4 to 11 January, and final completion on 17 or 18 January 2027

4 Functional Requirements

4.1 Core Product Features

1. **Bangla-first destination guides.** Users can explore destination profiles covering attractions, accommodation, food, transport, local practices, contacts, seasonality, and dated advisories in Bangla and English.
2. **Structured community reviews.** Reviews include travel date, traveller type, comfort level, text, overall rating, and category ratings. Review counts and moderation status remain visible.
3. **Transparent destination rating.** The platform uses a documented Bayesian score based on published overall ratings and a fixed semester prior. Hidden, rejected, and deleted reviews are excluded by tested query logic.
4. **Context-based cost planner.** Users receive an itemised BDT estimate based on party size, traveller type, dates, duration, comfort tier, transport, accommodation, meals, and selected activities. The result separates shared and per-person costs (Section 4.5).
5. **Offline travel pack.** Users can download public destination guidance, contacts, coordinates, advisories, and the generated estimate. The pack remains available in airplane mode after a successful download.
6. **Saved trip brief.** Users can save an estimate, free-text notes, and optional local contacts. This is a compact trip summary, not a day-by-day itinerary planner.
7. **Offline review draft.** A review written without connectivity remains on the device and can be submitted after reconnection. Retry requests use an idempotency key to prevent duplicates.
8. **Advisory freshness.** Every advisory stores its source, verification date, effective date, and validity date. Current, stale, and expired states are presented distinctly.
9. **Lean moderation and administration.** Authorised users manage destinations, translations, prices, advisories, review decisions, reports, and audit records.
10. **Privacy-aware account access.** Email verification controls review submission. The MVP does not collect real NID records, payment credentials, or unnecessary identity documents.

4.2 Future Product Features

The following capabilities belong to the product vision but are not required for semester acceptance:

- **Abhijatri Perks:** clearly disclosed partner benefits from approved resorts, restaurants, transport providers, and guides.
- **Vendor participation:** vendor registration, partner verification, reservation requests, ticket requests, and commission-based agency participation.
- **Find Tourmates:** verified organisers, join requests, capacity control, women-only options, participant visibility, private discussion, reporting, and blocking.
- **Advanced verification and payments:** real phone OTP, NID or student ID verification, verified-visit badges, real payments, refunds, and live inventory confirmation.
- **Platform expansion:** native mobile applications, advanced route planning, and context-aware machine learning once sufficient verified data exists.

4.3 User Roles

Table 2. User roles and permitted actions

Role	Permitted actions
Guest	Browse public destinations, switch language, generate estimates, and download public offline packs
Email-verified user	All guest actions plus saved trip briefs, review drafts, review submission, reporting, and account deletion request
Moderator	Review reports and publish, hide, reject, or flag content with a recorded reason
Administrator	Manage destinations, translations, prices, advisories, users, permissions, and audit records

4.4 Functional Requirement Catalogue

Table 3. Functional requirement catalogue

ID	Function	Input	Output or behaviour
FR01	Destination catalogue	Destination selection	Bilingual profile with attractions, transport, food, lodging, contacts, dates, and restrictions
FR02	Language selection	Bangla or English	Interface and available editorial content in the selected language
FR03	Account lifecycle	Email, password, and verification link	Verified session, reset, logout, and deletion request
FR04	Structured review	Rating, text, categories, and travel context	Pending review with a local draft retained until successful submission
FR05	Review moderation	Review and moderation decision	Published, hidden, rejected, or deleted state with actor, date, and reason
FR06	Review reporting	Published review and report reason	Moderator-visible report record with duplicate control
FR07	Destination rating	Eligible published overall ratings	Fixed-prior Bayesian score and visible review count
FR08	Cost planner	Party, traveller type, dates, comfort tier, transport, lodging, meals, and activities	Itemised BDT estimate with low, expected, and high values, per-person result, and confidence label
FR09	Pricing units	Source-dated price records	Calculation by person, room, vehicle, group, trip, day, night, meal, or entry
FR10	Offline pack	Destination and generated estimate	Versioned IndexedDB pack containing public guidance, contacts, coordinates, advisories, and costs
FR11	Saved trip brief	Estimate, notes, and optional contacts	Local record with a UUID and copy or delete action
FR12	Offline review draft	Review entered without connectivity	Local draft that survives refresh and session expiry
FR13	Retry-safe submission	Review and idempotency key	One server review for identical retries

Table 3 (continued)

ID	Function	Input	Output or behaviour
FR14	Pack update	Existing pack and newer manifest	Atomic replacement after the new pack passes validation
FR15	Advisory freshness	Source and validity dates	Current, stale, or expired state presented to the user
FR16	Administration	Authorised management action	Updated public data and immutable audit event
FR17	Storage control	Pack download or deletion request	Persistence status, storage notice, and local data removal

4.5 Abhijatri Cost Planner

Purpose. Travellers can find individual prices, but they rarely receive an estimate that explains how party size, travel dates, comfort tier, and shared costs change the total. The cost planner answers three practical questions before a trip: (i) can this group afford this trip, (ii) how should shared costs be divided fairly, and (iii) which choices (dates, comfort tier, transport) change the total most.

Approach. The MVP implements a deterministic rules engine. It does not use machine learning or probabilistic simulation, so every result can be reproduced by hand, reviewed, and tested. Each estimate is decision support, not a vendor quotation or a price guarantee.

Terminology. Two independent dimensions are used throughout. The **comfort tier** (economy, standard, or premium) is chosen by the user and selects which catalogue items apply. The **price range** (low, expected, or high) expresses the realistic spread of prices for the selected items within that tier.

4.5.1 Inputs and outputs

Table 4. Cost planner inputs and their effect on the calculation

Input	Values	Effect on the calculation
Destination and dates	Seeded destination; start and end date	Selects catalogue records and the season band of each chargeable day or night
Party	Party size n; traveller types (adult, student, child)	Sets the number of eligible travellers n_e for person-based items and the capacity division for shared items
Duration	Days d and nights m	Sets the number of chargeable periods
Comfort tier	Economy, standard, or premium	Selects the accommodation, transport, and meal records that apply
Choices	Transport mode, accommodation type, meal plan, activities	Includes or excludes cost categories and items

For every category the result shows the low, expected, and high cost, the pricing unit, the quantity used, the source date, and the confidence value. It also shows the group total, the per-person share, the split between shared and individual costs, the assumptions applied, and an overall confidence label.

4.5.2 Price catalogue

Each price record stores the destination, category, item, comfort tier, season applicability, pricing unit, capacity, low price, expected price, high price, source type, source reference, verification date, validity date, and confidence. Records must satisfy $p^L \leq p^E \leq p^H$, and room, vehicle, and group records must

state a capacity. Official sources take priority for fixed charges such as entry fees and permits. Recent moderated community reports are used for variable categories such as accommodation, food, and local transport.

4.5.3 Deterministic calculation

For each included category i and each range value $v \in \{L, E, H\}$, the engine computes

$$K_i^v \;=\; p_i^v \times q_i \times \sum_{\tau \in T_i} s(\tau), \tag{1}$$

where p_i^v is the unit price for range value v, q_i is the number of units required, T_i is the set of chargeable periods, and $s(\tau)$ is the season factor of period τ. The quantity and period rules are fixed per pricing unit (Table 5). Season factors are maintained in configuration for regular, weekend, peak, and public-holiday periods; fixed official charges always use $s(\tau) = 1$. Summing over periods, rather than applying one factor to the whole trip, correctly prices a trip that mixes weekday and weekend nights.

Table 5. Quantity and period rules by pricing unit

Pricing unit	**Units required q_i**	**Chargeable periods T_i**	**Typical use**
Per person	n_e	One occurrence	Intercity bus fare
Per entry	n_e	One per visit	Park or site entry fee
Per room	$\lceil n/c_i \rceil$	Each night (m)	Hotel or resort room
Per vehicle	$\lceil n/c_i \rceil$	Each day used (d)	Local jeep, CNG, or boat
Per group	$\lceil n/c_i \rceil$	Each day or one trip	Guide or permit escort
Per meal	n_e	Meals per day $\times\, d$	Restaurant meals
Per day / night	1	Each day or night	Daily service charge
Per trip	1	One occurrence	Reserved transfer

Here c_i is the capacity of one room, vehicle, or group unit, and $\lceil \cdot \rceil$ denotes ceiling division. The group totals and the per-person share are

$$T^v = \sum_i K_i^v, \qquad P^v = \frac{T^v}{n}. \tag{2}$$

Shared categories (rooms, vehicles, group services) are divided by party size only for the per-person view, and the result lists shared and individual amounts separately so the group can settle costs fairly. Calculations use unrounded values; displayed amounts are rounded to the nearest BDT 10.

4.5.4 Worked example

Table 6 applies Equation (1) to four students travelling to Cox's Bazar for three days and two nights (Thursday to Saturday) at the standard comfort tier. The first night is a regular night ($s = 1.00$); the second night and the last two days fall on the weekend ($s = 1.15$). The unit prices are indicative values chosen to demonstrate the rules; published estimates will use the source-dated catalogue records collected in tasks E02–E05.

Unit prices used (low / expected / high): bus 2,000 / 2,400 / 3,000 per person; room 2,200 / 3,000 / 4,000 per night; meal 180 / 250 / 350; vehicle 900 / 1,200 / 1,600 per day; entry 50. For example, the expected room cost is $3{,}000 \times \lceil 4/2 \rceil \times (1.00 + 1.15) = 12{,}900$. The shared share of the expected total (room and vehicle) is BDT 16,860, and the individual share is BDT 18,800.

Table 6. Worked example of the cost calculation (indicative prices, BDT)

Category	Unit and rule	q_i	$\sum s(\tau)$	Low	Expected	High	C_i
Intercity bus (return)	Per person, fixed	4	1.00	8,000	9,600	12,000	0.89
Hotel room, capacity 2	Per room, 2 nights	2	2.15	9,460	12,900	17,200	0.80
Meals, 3 per day	Per meal, 9 meals	4	9.00	6,480	9,000	12,600	0.73
Local vehicle, capacity 4	Per vehicle, 3 days	1	3.30	2,970	3,960	5,280	0.61
Park entry (official)	Per entry, fixed	4	1.00	200	200	200	0.87
Group total T^v				**27,110**	**35,660**	**47,280**	
Per person P^v				**6,780**	**8,920**	**11,820**	

4.5.5 Confidence and freshness

Each category receives a confidence value $C_i \in [0,1]$ computed from four documented components, each scaled to $[0,1]$:

$$C_i = 0.35A_i + 0.25F_i + 0.20R_i + 0.20G_i, \tag{3}$$

Authority carries the largest weight because official sources take priority for fixed charges; freshness follows because prices change with season and demand; the number of reports and their agreement share the remainder. Here A_i is source authority (official 1.0, verified operator 0.8, moderated community report 0.6), F_i is freshness (1.0 within the category refresh interval and 0.5 when stale), $R_i = \min(k_i/3,\, 1)$ for k_i independent reports, and $G_i = \max\big(0,\; 1-(p_i^H - p_i^L)/(2\,p_i^E)\big)$ measures agreement between reports. Overall confidence is weighted by the expected cost of each category:

$$C_{\text{overall}} = \frac{\sum_i K_i^E\, C_i}{\sum_i K_i^E}. \tag{4}$$

A score of at least 0.80 is labelled **High**, a score from 0.50 to below 0.80 is **Medium**, and a lower score is **Low**; a Low result is shown with an explicit verification warning. Table 7 derives the confidence values used in the worked example from Equation (3). The overall result is $C_{\text{overall}} = 28{,}024/35{,}660 = 0.79$, which is Medium: the stale local-vehicle record keeps the estimate just below High, and the result screen shows the corresponding warning.

Table 7. Derivation of category confidence for the worked example

Category	Source type	A_i	F_i	k_i	G_i	C_i
Intercity bus (return)	Verified operator fare	0.80	1.0	3	0.79	0.89
Hotel room	Moderated community	0.60	1.0	3	0.70	0.80
Meals	Moderated community	0.60	1.0	2	0.66	0.73
Local vehicle	Moderated community, stale	0.60	0.5	2	0.71	0.61
Park entry	Official notice	1.00	1.0	1	1.00	0.87

Freshness rules are applied before any calculation. Initial refresh intervals are 12 months for official fixed charges and 3 months for accommodation, food, and local transport. A record older than its refresh interval is **stale**: it may still be used, but with $F_i = 0.5$ and a visible warning. A record beyond its explicit validity date is **expired** and is excluded. The weights, factors, intervals, and thresholds above are initial configuration values; they are frozen with the rule specification (task E01), stored with a version number, and shown with every estimate.

4.5.6 Implementation and validation

The schedule follows the project Gantt chart (Section 7.3). The rule specification and worked examples are frozen first (E01). Source-dated price research covers four destinations during the second milestone (E02–E05), and the fifth destination is added during hardening (H01). The catalogue, rule engine, and result screens are then implemented (E06–E08), and the planner is tested against hand-calculated cases for every pricing unit, including odd party sizes, capacity one, stale records, expired records, and fixed charges that ignore season factors (E11–E12).

Ten independent trips are collected and sealed outside the seed catalogue. After the catalogue is frozen, the final report compares each expected estimate E with the actual in-scope cost A using the absolute percentage error $|E-A|/A$ per category and in total, the mean absolute percentage error (MAPE), and coverage, defined as the share of trips whose actual cost lies within $[T^L, T^H]$. The planner is compared with a simple baseline of one average per-person per-day cost multiplied by $n \times d$. The proposed acceptance target is a lower MAPE than the baseline and coverage of at least 7 of 10 trips. This scope is implementable with FastAPI, PostgreSQL, and standard arithmetic.

4.6 Primary Use Cases


The use case model (Figure 1) shows the complete Abhijatri PWA system boundary, its four actors, and the use cases grouped by functional domain. Table 8 summarises the scope of the diagram. Packages 4 (booking) and 6c (payment verification) are demonstration-only and lie outside semester acceptance, consistent with the scope decision. The editable source model is available online: **open the original use case diagram in Lucidchart**.

Table 8. Scope of the use case model

Element	Content
Actors	Guest, email-verified user, moderator, and administrator
Core packages	Supporting (language and account), 1. Cost Estimator, 2. Offline, 3. Review, 5. Community, Administration, 6a. Advisory and offline-pack verification, 6b. Email and account verification
Demonstration only	4. Booking (demo reservation) and 6c. Payment verification (demo). No money transfer and no live inventory
System boundary	Abhijatri PWA and its controlled management functions
Notation	Solid line: actor association. Dashed arrow labelled «include»: mandatory sub-behaviour. Dashed arrow labelled «extend»: optional or conditional behaviour. Bold ellipse: primary use case of a package
Naming notes	**Manage Prices** maintains cost-planner catalogue records; **Manage Packages & Prices** maintains demonstration booking packages only. **Record Audit Event** (advisory re-verification) and **Record Immutable Audit Event** (administration) write to the same append-only audit log

Use Case Diagram of the Abhijatri System

Figure 1. Abhijatri system use case model (UML). Packages 4 and 6c are demonstration-only.

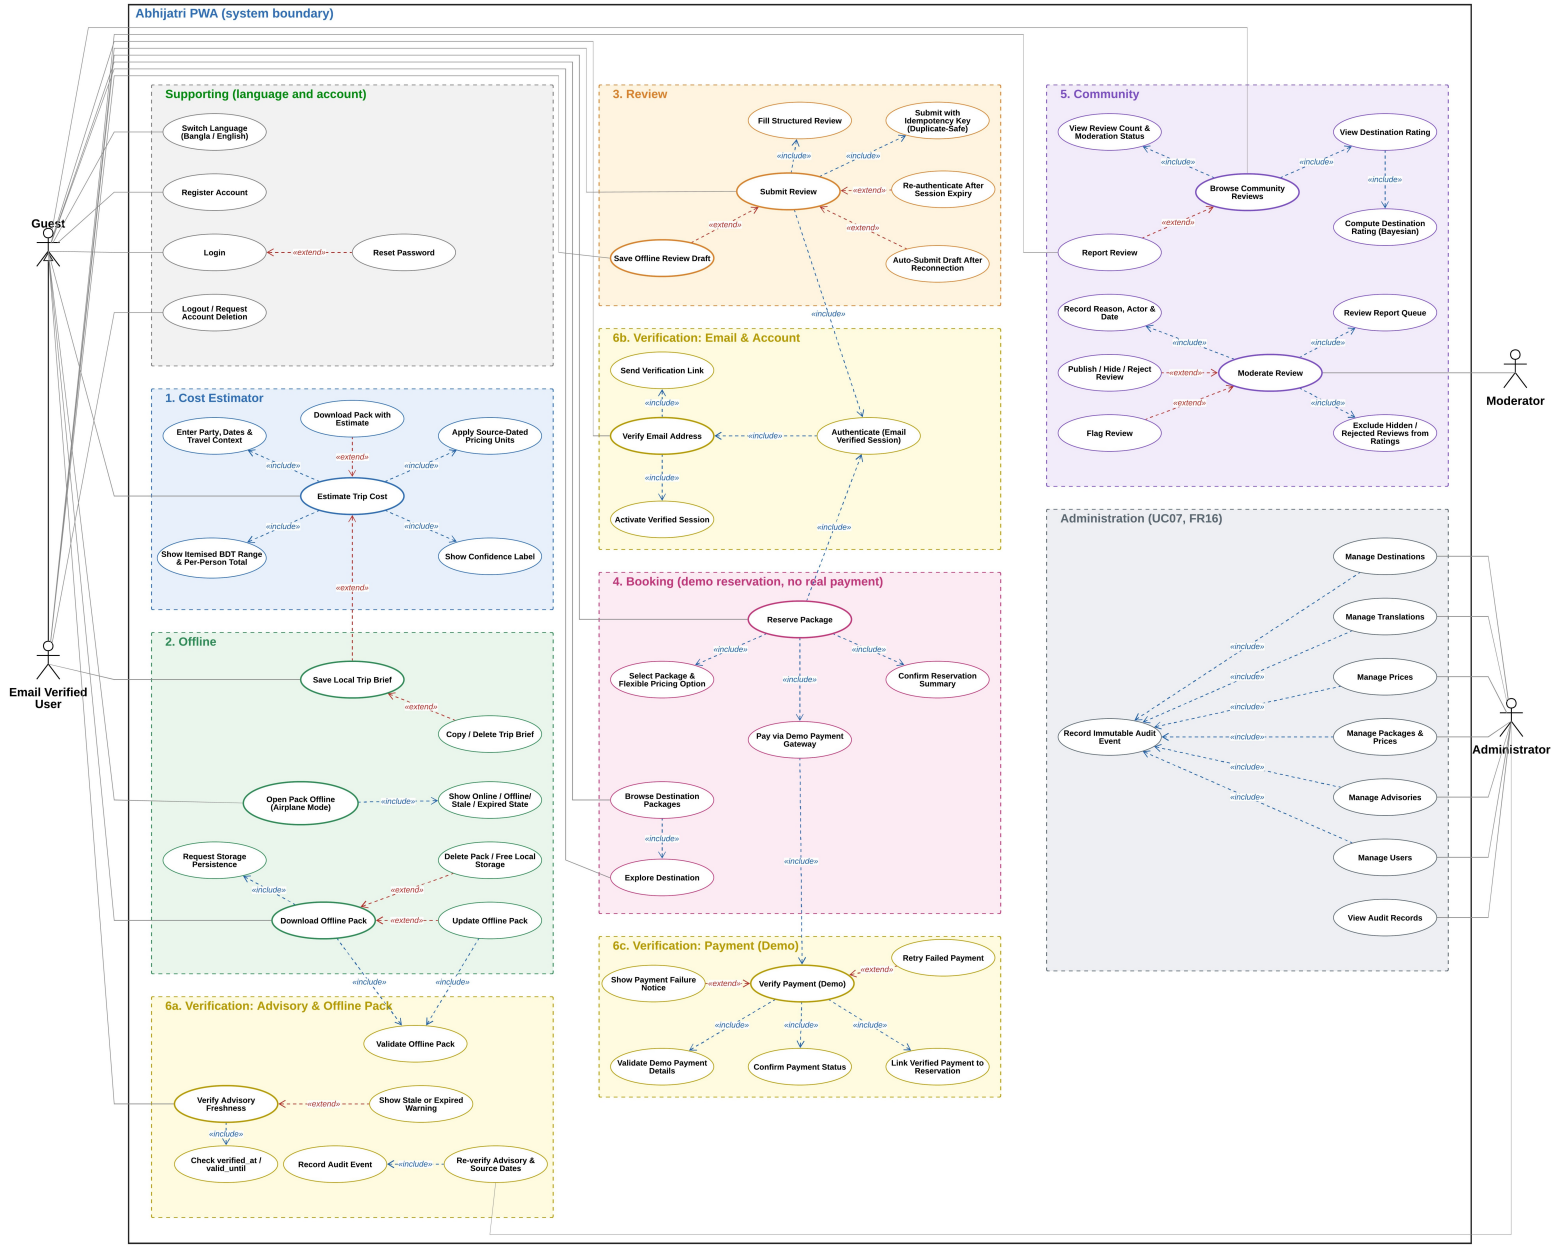

Original diagram: **open the editable use case model in Lucidchart**

4.7 Representative User Stories

Table 9 lists representative user stories in the standard role–goal–benefit form, each traced to the functional requirements that satisfy it.

Table 9. Representative user stories with requirement traceability

ID	As a ...	I want ...	So that ...	Traces to
US1	Bangla-speaking traveller	destination guidance in Bangla	I can use the service without depending on English content	FR01, FR02
US2	Student travelling with friends	shared and per-person costs shown separately	we can divide the budget fairly	FR08, FR09
US3	Traveller entering a weak-network area	contacts, coordinates, advisories, and my estimate available offline	I can still act when the network fails	FR10, FR17
US4	Reviewer	my offline draft to survive session expiry	I can authenticate and submit without rewriting it	FR12, FR13
US5	Moderator	hidden and rejected reviews excluded from ratings	invalid content does not influence the score	FR05, FR07
US6	Administrator	stale prices and expired advisories identified	outdated data is never presented as current	FR15, FR16

4.8 MVP Exclusions

The semester acceptance scope excludes real payments, refunds, live inventory, vendor self-registration, real phone OTP, NID collection, student ID processing, verified-visit badges, group tours, private chat, traveller monitoring, day-by-day itinerary planning, route optimisation, native mobile applications, automated translation, and machine-learning recommendations.

5 Non-functional Requirements

Table 10. Non-functional requirements and acceptance measures

Category	Requirement and acceptance measure
Performance	Core destination text becomes usable within 5 seconds under the agreed Fast 3G throttle on the target low-end Android device. A downloaded pack opens within 2 seconds. Catalogue, review, and estimator APIs remain below 2 seconds at the 95th percentile under a 50-user academic load test, and the API layer sustains at least 20 requests per second at that load without errors.
Security and access control	Argon2id password hashing, opaque server-side sessions, HttpOnly and Secure production cookies, CSRF protection, input validation, least-privilege roles, rate limits, and audit logs. Sensitive credentials and identity records never enter offline packs.
Reliability and availability	Identical retries do not create duplicate reviews. Interrupted pack updates preserve the last complete version. The deployed pilot includes a database backup and one restore test. Online, offline, stale, and expired states are distinct. Target availability is at least 99% during the pilot and demonstration windows, measured by an external uptime check.
Scalability	Stateless FastAPI application layer, PostgreSQL indexes, pagination, and bounded queries. The architecture permits multiple API instances later. The semester load target is 50 concurrent virtual users.

Table 10 (continued)

Category	Requirement and acceptance measure
Usability and accessibility	Bangla is the default locale. Forms have labels, keyboard access, clear errors, readable contrast, and tested Bengali conjunct rendering. Applicable WCAG 2.2 AA criteria are evaluated with at least eight users.
Maintainability	Modular React and FastAPI components, database migrations, API documentation, coding conventions, code review, and automated unit and integration tests. Each content category has an owner and an update interval.
Portability	Current Chromium-based Android browsers and modern desktop browsers. Safari limitations are documented and tested where a device is available.
Privacy	Minimum account and pilot data, informed consent, optional personal contacts kept local to the device, defined retention periods, and support for account deletion and review-removal requests.

6 Stakeholders

Table 11. Stakeholders, interests, and engagement

Stakeholder	Interest or authority	Engagement
Course instructor and evaluators	Approve scope, review progress, and evaluate the outcome	Proposal, biweekly reports, demonstrations, and final evidence
Team ChoturMatra	Design, implement, test, document, and maintain the MVP	Shared repository, issue tracking, reviews, and demonstrations
Travellers and tourists	Use destination, estimate, offline, and review functions	Usability sessions and pilot feedback
Local residents and experienced travellers	Provide local context and cost reports	Consent-based pilot and source verification
Moderators and administrators	Protect content quality and maintain dated information	Moderation and administration tests
Destination authorities	Provide restrictions, permits, and safety notices	Dated official public sources
Future vendors and agencies	Provide services and future commercial participation	Future onboarding and commission policy

7 Timeline and Milestones

The schedule follows the fixed dates agreed by the team. Early completion is allowed, but acceptance dates are not moved without instructor approval.

Table 12. Fixed milestones and acceptance evidence

Date	Gate	Milestone	Acceptance evidence
2 November 2026	M1	Major feature accepted	Destination information, structured reviews, bilingual interface, moderation, and offline support operate as one flow
7 December 2026	M2	Significant progress	Approximately 50 to 60 percent of the fixed MVP is accepted, including estimator integration and evidence
3 January 2027	G1	Testing-entry gate	Frozen build, test data, requirement traceability, environment, and procedures are approved
4–11 January 2027	M3	Formal testing	Full-flow, non-functional, usability, regression, defect, and exit records are complete
17 or 18 January 2027	M4	Final completion	Release candidate, report, evidence archive, deployment notes, and demonstration are complete

7.1 Formal Testing Phase

Table 13. Formal testing activities and required records

Area	Schedule	Activities and required records
Test leadership	Before execution	Irfan leads the master test plan, test-case register, execution record, and exit recommendation. Every requirement is mapped to test IDs.
Test-case record	4–11 January	Record ID, requirement, preconditions, data, steps, expected result, actual result, status, evidence, defect, severity, owner, and retest result.
Destination and estimate	4–11 January	Browse a seeded destination, switch language, read dated guidance, and generate context-specific estimates.
Offline flow	4–11 January	Save a trip brief, download a pack, use airplane mode, reopen essential information, reconnect, and verify refresh status.
Review and moderation	4–11 January	Submit an offline draft, retry safely, moderate it, and verify rating exclusions.
Access and failures	4–11 January	Test roles, pricing units, stale warnings, duplicate requests, network failures, and review reporting.
Non-functional testing	4–11 January	Test throttled 2G and 3G, airplane mode, low-end Android, Bangla rendering, accessibility, storage refusal, cache updates, privacy, and response times.
Usability	4–11 January	Test at least eight consenting users, including a Bangla-preferring and a less technical participant.
Defect management	4–11 January	Record reproducible evidence, assign severity and owner, retest fixes, and run affected-flow regression.
Exit criteria	By 11 January	Every in-scope requirement has a status. No blocker or critical defect remains in the core flow. Residual lower-severity issues are documented.

7.2 Progress Reporting

Each biweekly report records planned work, completed work, evidence, measured progress, defects, blocked items, changed assumptions, accepted work, and approved scope changes.

7.3 Project Gantt Chart

The operational schedule contains 74 tasks in six phases, with dependencies, primary owners, effort points, and five fixed gates. Table 14 summarises the phases, Table 15 shows that primary effort is balanced at 87 points (25 percent) per member, and Figures 2–4 present the complete task-level chart. Acceptance evidence and risk notes for every task are maintained in the live schedule: **open the live 74-task implementation schedule in Google Sheets**.

Reading the chart. Grey bars span each task from its start day to its end day; black diamonds mark milestones and gates; dark summary bars show the span of each phase; vertical dashed lines mark the fixed dates M1 (2 Nov), M2 (7 Dec), G1 (3 Jan), M3 (11 Jan), and M4 (17 Jan). Week columns are labelled with the date of each Monday. Effort is given in points; support members are listed in the live schedule.

Table 14. Schedule summary by phase

Phase	Window	Tasks	Effort	Exit gate
Foundation	12–16 Oct 2026	7	29	Scope, architecture, test plan
M1: Destination, reviews, offline	15 Oct – 2 Nov 2026	21	99	M1, 2 Nov 2026
M2: Cost estimator and checkpoint	3 Nov – 7 Dec 2026	15	75	M2, 7 Dec 2026
Hardening and test readiness	8 Dec 2026 – 3 Jan 2027	12	60	G1, 3 Jan 2027
Formal testing	4–11 Jan 2027	10	48	M3, 11 Jan 2027
Completion and final delivery	12–18 Jan 2027	9	37	M4, 17/18 Jan 2027
Total	**14 weeks**	**74**	**348**	

Table 15. Primary-owner workload balance

Owner	Role	Tasks	Effort	Share
Shahriar Islam	Project leader, content, moderation	22	87	25%
Abdullah Bin Sorwar Choudhury	Frontend, bilingual interface, offline	17	87	25%
Syed Muhtasim Alam	Backend, data, security	17	87	25%
Md. Irfan Iqbal	SQA, test management	18	87	25%
Total		**74**	**348**	**100%**

Figure 2. Implementation Gantt chart, part 1 of 3: foundation and first major feature (M1)
Live schedule: **open the Gantt chart in Google Sheets**

ID	Task / deliverable	Owner	Eff.	Start	End	Depends on
Foundation				**12 Oct – 16 Oct**		**7 tasks, 29 pts**
F01	Freeze first-release scope and acceptance gates	Shahriar	4	12 Oct	13 Oct	–
F02	Define architecture, database schema and API contract	Muhtasim	6	12 Oct	14 Oct	F01
F03	Create bilingual information architecture and UI component plan	Abdullah	4	12 Oct	14 Oct	F01
F04	Create master test plan and requirement traceability matrix	Irfan	4	12 Oct	15 Oct	F01
F05	Define source/date/licence template for destinations	Shahriar	3	12 Oct	14 Oct	F01
F06	Set up repositories, CI checks and shared environments	Muhtasim	5	12 Oct	15 Oct	F02
F07	Create privacy, access-control and cache-safety checklist	Irfan	3	13 Oct	16 Oct	F02
M1: Destination, reviews, bilingual interface and offline support				**15 Oct – 2 Nov**		**21 tasks, 99 pts**
R01	Prepare one complete bilingual seeded destination	Shahriar	5	15 Oct	22 Oct	F05
R02	Build destination, advisory and contact data services	Muhtasim	5	15 Oct	21 Oct	F02, R01
R03	Build bilingual destination list and detail screens	Abdullah	5	15 Oct	22 Oct	F03, R02
R04	Implement registration, email verification, sign-in/out and reset	Muhtasim	5	15 Oct	22 Oct	F02, F07
R05	Build account, verification and session screens	Abdullah	4	18 Oct	23 Oct	R04
R06	Finalize review fields, lifecycle and moderation policy	Shahriar	4	15 Oct	19 Oct	F01, F04
R07	Implement structured review CRUD, ownership and pagination	Muhtasim	6	18 Oct	26 Oct	R04, R06
R08	Implement Bayesian score and rating exclusion logic	Muhtasim	4	22 Oct	27 Oct	R07
R09	Build review form, list, filters and author controls	Abdullah	6	20 Oct	27 Oct	R05, R07
R10	Build moderation queue, reason capture and audit view	Shahriar	5	20 Oct	27 Oct	R06
R11	Implement review reporting, moderation actions and audit log	Muhtasim	5	22 Oct	28 Oct	R07, R10
R12	Create installable PWA shell and cache public destination views	Abdullah	5	19 Oct	25 Oct	R03
R13	Store versioned destination pack and published-review snapshot in IndexedDB	Abdullah	6	23 Oct	30 Oct	R12, R14
R14	Implement pack manifest, version and freshness endpoints	Muhtasim	4	22 Oct	27 Oct	R02
R15	Implement offline review drafts and idempotent reconnect submission	Abdullah	5	25 Oct	31 Oct	R09, R13, R16
R16	Implement server-side idempotency-key storage and expiry	Muhtasim	3	24 Oct	28 Oct	R07
R17	Execute account, review, moderation and rating tests	Irfan	6	20 Oct	31 Oct	R04, R07, R11
R18	Test airplane mode, weak network, Bangla and storage failure	Irfan	6	23 Oct	1 Nov	R12, R15
R19	Run integration, defect triage and scope control	Shahriar	5	25 Oct	1 Nov	R03, R11, R13
R20	Run M1 acceptance regression and prepare test summary	Irfan	4	30 Oct	2 Nov	R17–R19
M1	**Major feature accepted: destination + reviews + bilingual offline support**	**Shahriar**	**1**	**2 Nov**	**2 Nov**	**R20**

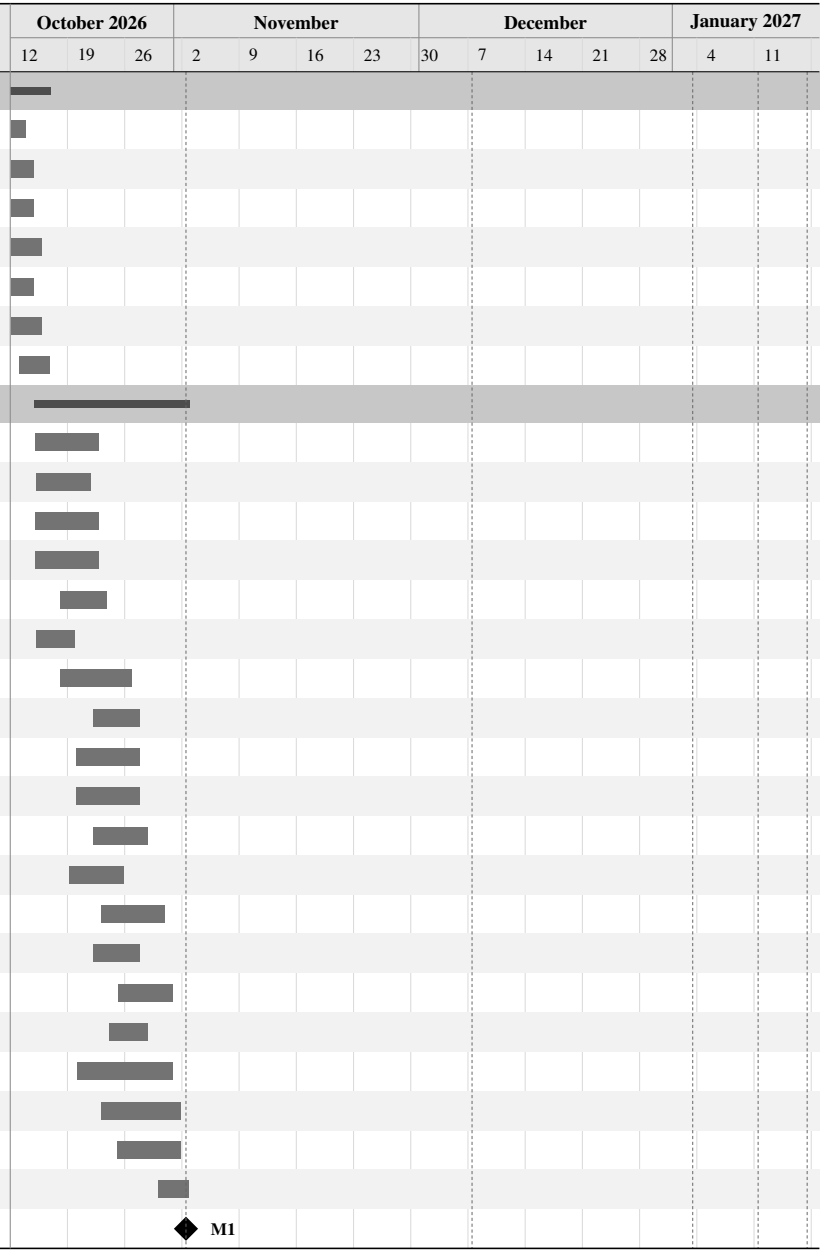


Figure 3. Implementation Gantt chart, part 2 of 3: cost estimator, 50–60% checkpoint (M2), and hardening
Live schedule: **open the Gantt chart in Google Sheets**

ID	Task / deliverable	Owner	Eff.	Start	End	Depends on
M2: Cost estimator and 50–60% progress checkpoint				**3 Nov – 7 Dec**		**15 tasks, 75 pts**
E01	Freeze rule engine, pricing units, confidence and scope	Shahriar	5	3 Nov	8 Nov	M1
E02	Research destination A prices and advisories	Shahriar	4	3 Nov	14 Nov	E01
E03	Research destination B prices and advisories	Abdullah	4	3 Nov	14 Nov	E01
E04	Research destination C prices and advisories	Muhtasim	4	3 Nov	14 Nov	E01
E05	Research destination D prices and advisories	Irfan	4	3 Nov	14 Nov	E01
E06	Implement pricing catalogue, units, season and freshness model	Muhtasim	6	9 Nov	22 Nov	E01–E05
E07	Implement itemized rule engine and confidence calculation	Muhtasim	7	16 Nov	29 Nov	E06
E08	Build traveller-context input and itemized result screens	Abdullah	7	16 Nov	30 Nov	E01, E07
E09	Save estimate, notes and optional contacts; include in offline pack	Abdullah	5	23 Nov	3 Dec	E08, R13
E10	Build minimal price/advisory maintenance interface	Shahriar	6	16 Nov	30 Nov	E06
E11	Create hand-calculated scenarios, baseline and held-out protocol	Irfan	6	9 Nov	24 Nov	E01
E12	Execute calculation, stale-data and confidence tests	Irfan	6	23 Nov	4 Dec	E07, E11
E13	Integrate estimator, saved brief, review and offline flows	Abdullah	5	28 Nov	5 Dec	E08–E10
E14	Run progress audit, defect triage and evidence pack	Shahriar	5	30 Nov	6 Dec	E10, E12
M2	**Significant progress checkpoint: 50–60% complete**	**Shahriar**	**1**	**7 Dec**	**7 Dec**	**E14**
Hardening and testing-entry readiness				**8 Dec – 3 Jan**		**12 tasks, 60 pts**
H01	Add and quality-check remaining MVP destinations	Shahriar	6	8 Dec	20 Dec	M2
H02	Improve review transparency, filtering and rating explanation	Abdullah	5	8 Dec	18 Dec	M2
H03	Harden cache versioning, invalidation and storage recovery	Abdullah	6	8 Dec	24 Dec	M2
H04	Add pagination, structured errors, logging and retry safety	Muhtasim	6	8 Dec	22 Dec	M2
H05	Harden sessions, CSRF/origin policy and role permissions	Muhtasim	6	15 Dec	27 Dec	F07, H04
H06	Polish moderation and source-maintenance workflow	Shahriar	5	15 Dec	27 Dec	E10, H02
H07	Expand automated regression and smoke-test suite	Irfan	5	8 Dec	27 Dec	M2
H08	Run pilot with at least eight consenting participants	Irfan	5	15 Dec	29 Dec	H01
H09	Fix keyboard, readability, responsive and Bangla-rendering issues	Abdullah	5	21 Dec	2 Jan	H02, H08
H10	Prepare frozen test build, data, environment and procedures	Irfan	5	28 Dec	3 Jan	H03–H05, H07
H11	Prepare deployment, recovery, setup and operator documentation	Shahriar	5	21 Dec	3 Jan	H04, H06
G1	**Testing-entry readiness review**	**Shahriar**	**1**	**3 Jan**	**3 Jan**	**H10**


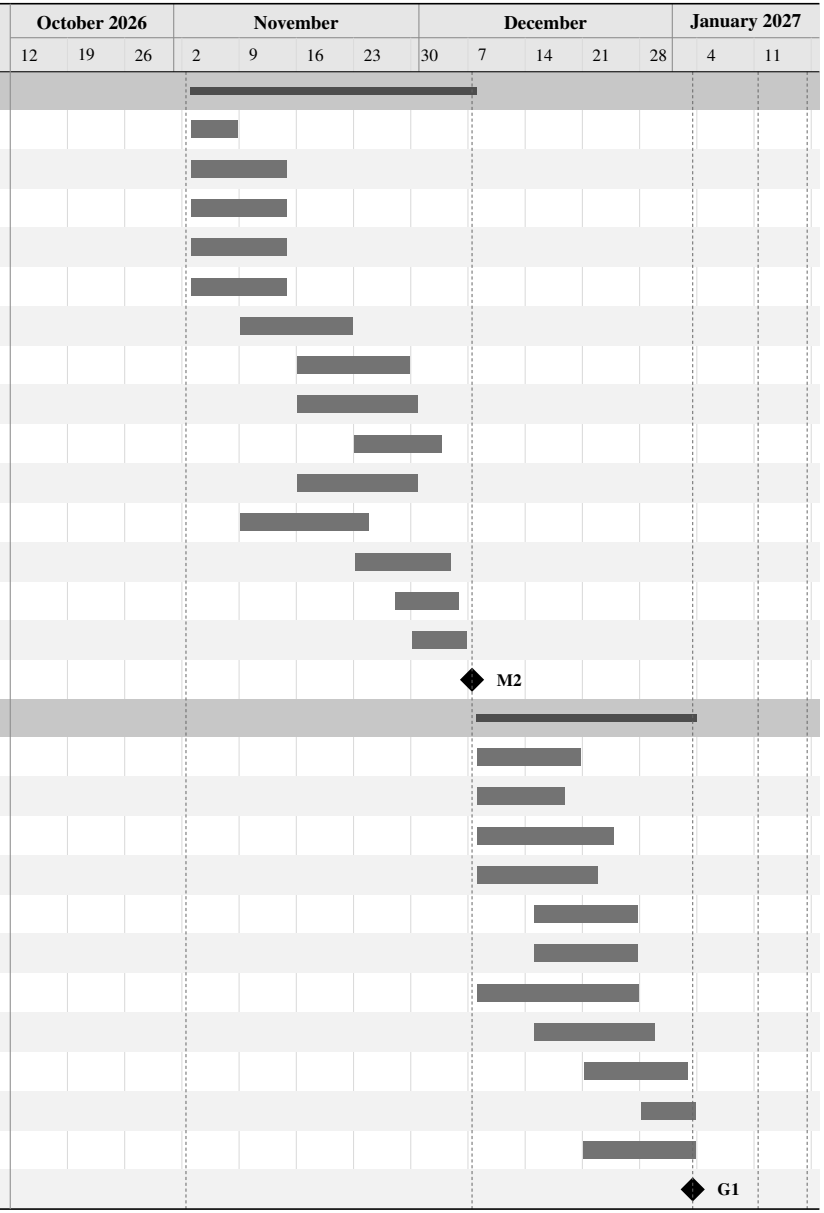


Figure 4. Implementation Gantt chart, part 3 of 3: formal testing (M3) and final completion (M4)
Live schedule: **open the Gantt chart in Google Sheets**

ID	Task / deliverable	Owner	Eff.	Start	End	Depends on
Formal testing				**4 Jan – 11 Jan**		**10 tasks, 48 pts**
T01	Freeze build and brief testers on data, environment and defects	Shahriar	3	4 Jan	4 Jan	G1
T02	Finalize RTM, master register and execution records	Irfan	5	4 Jan	5 Jan	H10
T03	Execute destination-estimate-offline-review full flow	Irfan	6	5 Jan	8 Jan	T02
T04	Execute 2G/3G, airplane, device, accessibility and privacy tests	Irfan	6	5 Jan	9 Jan	T02
T05	Resolve assigned UI, bilingual and offline defects	Abdullah	6	6 Jan	10 Jan	T03
T06	Resolve assigned API, security and data defects	Muhtasim	6	6 Jan	10 Jan	T03
T07	Resolve data, advisory and moderation defects	Shahriar	5	6 Jan	10 Jan	T03
T08	Retest fixes and run affected-flow regression	Irfan	6	8 Jan	11 Jan	T05–T07
T09	Complete SQA summary and exit recommendation	Irfan	4	11 Jan	11 Jan	T08
M3	**Formal testing completed**	**Irfan**	**1**	**11 Jan**	**11 Jan**	**T09**
Completion and final delivery				**12 Jan – 18 Jan**		**9 tasks, 37 pts**
C01	Close remaining approved UI defects and freeze client	Abdullah	5	12 Jan	15 Jan	M3
C02	Close remaining approved backend defects and freeze services	Muhtasim	5	12 Jan	15 Jan	M3
C03	Freeze destination, price and advisory content	Shahriar	4	12 Jan	15 Jan	M3
C04	Run release-candidate smoke test and verify evidence archive	Irfan	5	15 Jan	16 Jan	C01–C03
C05	Finalize report, setup guide, limitations and maintenance plan	Shahriar	5	12 Jan	16 Jan	M3
C06	Prepare and rehearse timed final demonstration	Shahriar	4	15 Jan	17 Jan	C04
C07	Prepare stable demo build and backup deployment	Muhtasim	4	15 Jan	17 Jan	C02, C04
C08	Prepare final screenshots and bilingual demo data	Abdullah	4	15 Jan	17 Jan	C01, C03
M4	**Final project completion**	**Shahriar**	**1**	**17 Jan**	**18 Jan**	**C04, C06–C08**

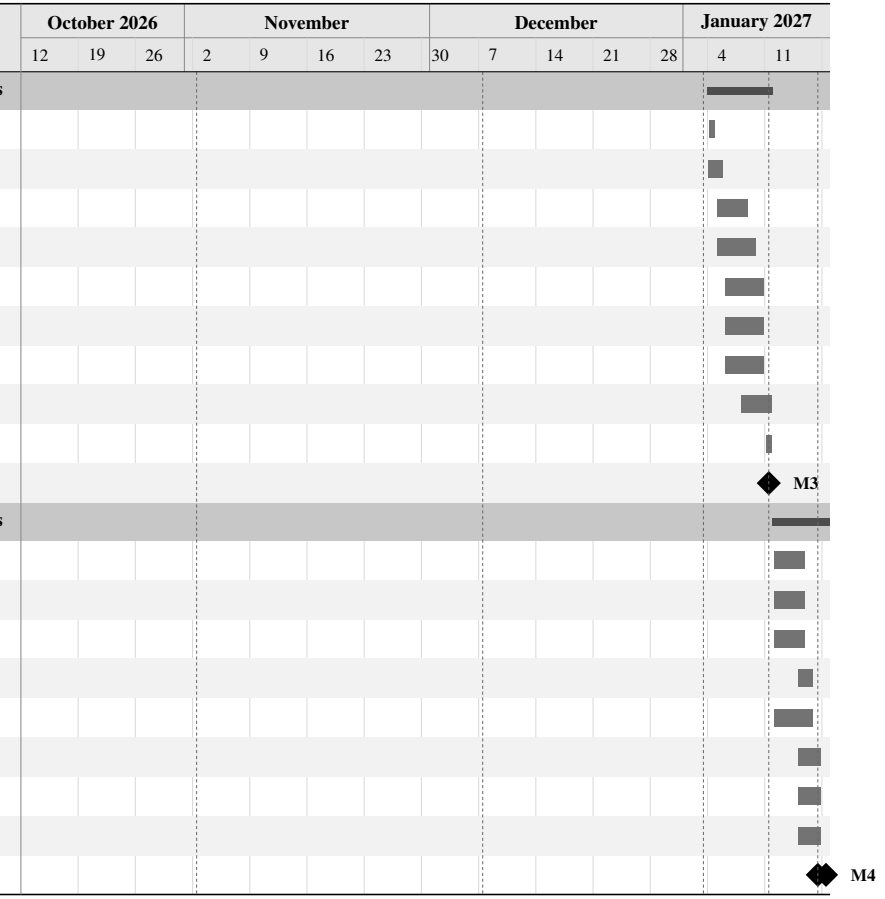

8 Risk Assessment

Table 16. Risk register with early warnings and mitigation

Risk	Level	Early warning	Mitigation and owner
Scope growth	High	New features requested during a cycle	Freeze the semester capabilities. Any addition replaces work of equal effort. Owner: Shahriar.
Insufficient destination or price data	High	Missing sources or conflicting values	Begin research in the first cycle. Store provenance, date, unit, tier, and confidence. Owners: all content owners.
Weak estimator accuracy	High	Large error on development cases	Use ranges, transparent rules, a baseline, and sealed held-out trips. Owners: Shahriar and Irfan.
Stale safety information	High	Advisory lacks a current official source	Store verification and validity dates. Recheck before publication and demonstrations. Owners: destination owners.
Offline storage eviction	Medium	Persistence is refused or a pack disappears	Show status, re-download, and delete controls. Test on real devices. Owners: Abdullah and Irfan.
Authentication delay	Medium	Account API misses the planned cycle	Continue the guest destination and pack slice. Complete accounts early in the next cycle. Owner: Muhtasim.
Team unavailability	High	Missed review or unmerged work	Maintain shared documentation, small reviewed changes, tests, and a backup owner for each module. Owner: Shahriar.
Privacy or security defect	High	Sensitive data appears in logs, cache, or pack	Apply data minimisation, network-only private APIs, security tests, and a release gate. Owners: Muhtasim and Irfan.
Bangla rendering failure	Medium	Broken conjuncts or unreadable wrapping	Use system-font fallback and a device-version test matrix. Owner: Abdullah.
Low pilot participation	Medium	Fewer than eight usable participants	Recruit early and maintain backup participants. Owner: Irfan.
Copyright issue	Medium	Image or source has unclear permission	Use owned or openly licensed images and record licences. Owner: each content owner.
Deadline pressure	High	The 7 December target or testing entry is at risk	Review scope at the checkpoint and protect the fixed testing and final dates. Owners: Shahriar and team.

9 Feasibility Study

9.1 Technical Feasibility

The selected technologies match the team roles, and each member owns the part of the stack that matches their existing strengths: Abdullah the React and PWA frontend, Muhtasim the FastAPI and PostgreSQL backend, Irfan test automation and device testing, and Shahriar content, rules, and integration. The Foundation phase and the first destination slice also act as an early technical check of the full stack before the first milestone. React and TypeScript support the bilingual frontend. FastAPI supports the API layer. PostgreSQL provides authoritative relational storage. Workbox manages the versioned application shell. IndexedDB through Dexie stores downloaded packs, saved trip briefs, and review drafts. Authenticated API responses are excluded from public service-worker caches.

The MVP avoids dependencies on real payments, SMS gateways, NID verification, live inventory, and native application packaging. The highest-risk capability, offline access, is tested with one complete destination before the first milestone. The architecture is therefore achievable by the team within the semester.

9.2 Economic and Financial Feasibility

The MVP uses open-source frameworks and existing student hardware. The figures below are planning allowances, not quotations.

Table 17. Semester cost allowance

Cost category	Estimated BDT	Basis
Development frameworks and database	0	Open-source software
Existing laptops and Android test phones	0	Team-owned equipment
Test connectivity, calls, and data collection	1,500	Pilot and source-verification allowance
Optional domain and short-term hosting	2,500	Used only if an external demonstration requires it
Contingency	2,000	Unexpected testing or deployment expense
Planning ceiling	**6,000**	Maximum proposed semester allowance

The future business model can include vendor subscriptions, booking commissions, clearly labelled sponsorship, and optional premium services. Sponsorship must not affect ratings or moderation. With a maximum direct cost of BDT 6,000, open-source tooling, and existing equipment, the project delivers a working, tested product and a reusable price and content catalogue at very low cost, so the investment is clearly justified.

9.3 Schedule and Time Feasibility

The Gantt chart assigns dependencies, evidence, risk notes, and effort to each task, and workload is balanced at 87 primary effort points per member. The first complete vertical slice is due on 2 November. The 7 December checkpoint leaves time to reduce destination quantity before reducing quality. Formal testing has a protected eight-day window, followed by a final correction and release period.

If work falls behind, the team will remove future-phase functions before changing core acceptance criteria. Real booking, real payment, group tours, and advanced verification remain outside the semester dependency chain.

9.4 Operational and Ethical Feasibility

Pilot participation is voluntary and uses a short consent notice. The project does not collect real NID records, payment credentials, or unnecessary personal documents. Optional contacts remain local to the user's device. Abhijatri will not present itself as an emergency-response or traveller-monitoring service. Restrictions and advisories must be verified again before publication or demonstration.

9.5 Feasibility Conclusion

Abhijatri is feasible as a semester project if the team preserves the MVP boundary and treats commercial and social expansion as future work. The selected technology is available, direct academic cost is limited, risk is tested early, and the schedule includes formal acceptance evidence.
